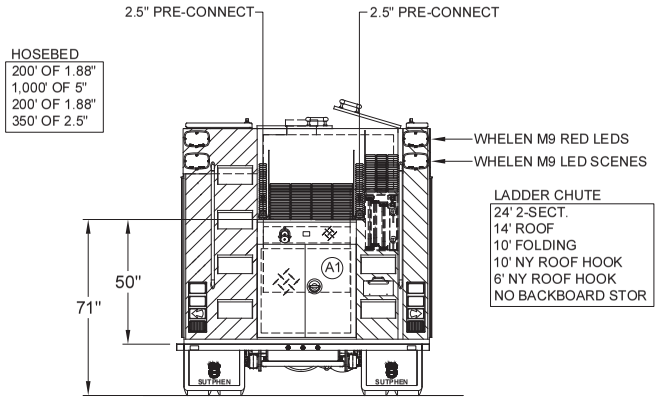

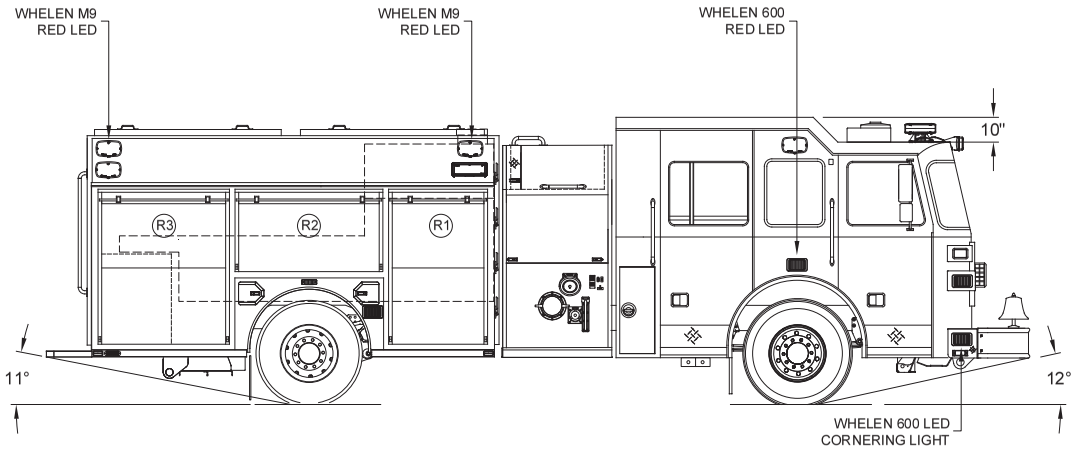

LEFT SIDE COMPARTMENTATION				
COMPT	DOORS	OPENING DIMENSIONS	INSIDE DIMENSIONS	VOLUME
L1	ROLL-UP	37"w X 56 7/8"h	43"w X 66"h X 27 1/4"d	40 CU. FT.
L2	ROLL-UP	57"w X 27 5/8"h	61 1/2"w X 36 1/2"h X 27 1/4"d	30 CU. FT.
L3	ROLL-UP	50"w X 56 7/8"h	53 1/2"w X 66"h X 27 1/4"d	55 CU. FT.

RIGHT SIDE COMPARTMENTATION				
COMPT	DOORS	OPENING DIMENSIONS	INSIDE DIMENSIONS	VOLUME
R1	ROLL-UP	37"w X 50 7/8"h	43"w X 66"h X 27 1/4"d (10 1/2"d upper)	26 CU. FT.
R2	ROLL-UP	57"w X 21 5/8"h	61 1/2"w X 36 1/2"h X 10 1/2"d	13 CU. FT.
R3	ROLL-UP	50"w X 50 7/8"h	53 1/2"w X 66"h X 27 1/4"d (10 1/2"d upper)	43 CU. FT.

REAR STEP COMPARTMENTS				
COMPT	DOORS	OPENING DIMENSIONS	INSIDE DIMENSIONS	VOLUME
A1	HINGED	37 1/2"w X 32.8"h	40"h X 40"w X 31"d	27 CU. FT.

TOTAL: 234 CU. FT.

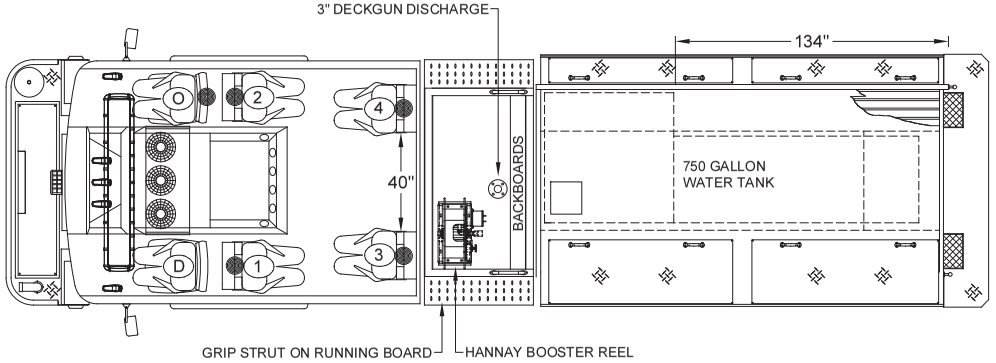

TWO-TONE CAB
PAINT BREAK OPTION #3
WHITE OVER YELLOW

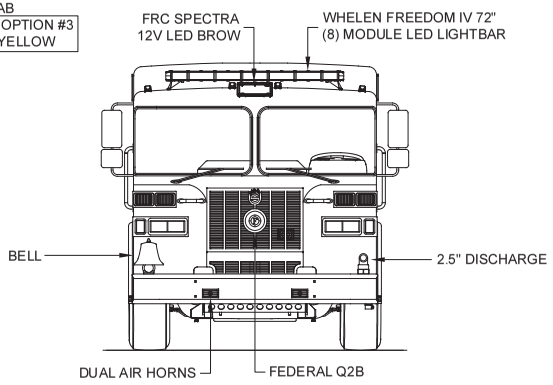

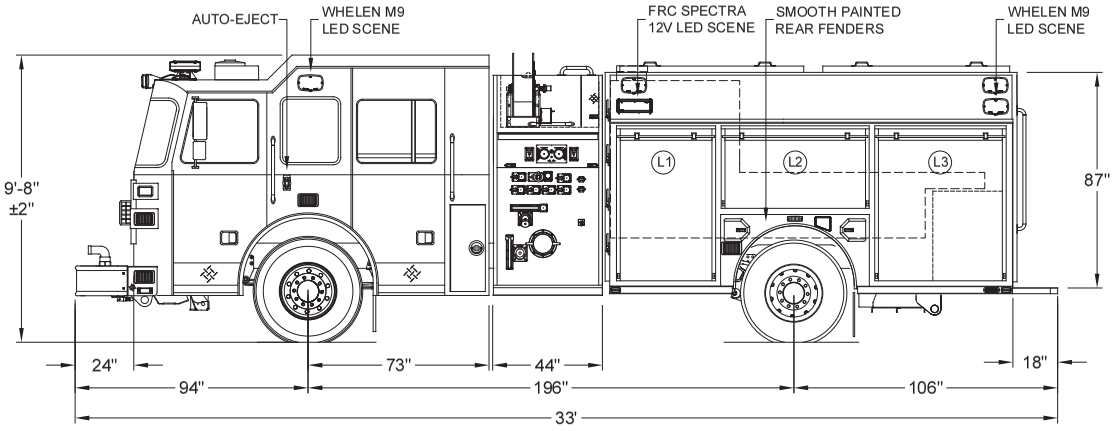

DIMENSIONS SHOWN ON THIS DRAWING ARE APPROXIMATE AND ARE SUBJECT TO MINOR DEVIATIONS DURING CONSTRUCTION.	CUSTOMER APPROVAL	F	SPECTRAS MOVED TO FRONT SIDE BODY CORNERS ; PAIR OF M9 SCENE LIGHTS ADDED TO REAR SIDE BODY CORNERS	RM	01/17/19	DRAWN BY: J.MORGAN	SUTPHEN
IN THE EVENT OF A DISCREPANCY BETWEEN THE SUTPHEN SPECIFICATIONS AND DRAWING, THE SUTPHEN SPECIFICATIONS SHALL PREVAIL.	NAME:	E	CLARIFIED THAT CUSTOMER WANT AIR PUMP SHIFT	JM	11/21/18	DATE: 07/16/18	CITY OF ALABASTER ALABASTER, AL
DRAWING IS FOR REFERENCE ONLY. SOME ITEMS PROPOSED MAY NOT BE SHOWN OR NOTED.	TITLE:	D	LOCATION FOR JENSEN RADIO HEAD IN CAB ; COLOR FOR REAR CHEVRONS DETERMINED	RM	10/23/18	MFG. FACILITY: DUBLIN	CUSTOM PUMPER - MODIFIED PA-12 BODY
	DATE:	C	MULTIPLE UPDATES AND CLARIFICATIONS - SEE SO REVISION EMAIL FOR FULL LIST	RM	10/19/18		DWG. NO.: HS-6260
		REV.	DESCRIPTION	BY	DATE		

THIS PRINT IS PROVIDED ON A RESTRICTED BASIS AND IS NOT TO BE USED IN ANY WAY DETRIMENTAL TO THE INTEREST OF SUTPHEN CORPORATION.
